


### NPARIH REFURBISHMENTS - ANNUAL ACHIEVEMENTS

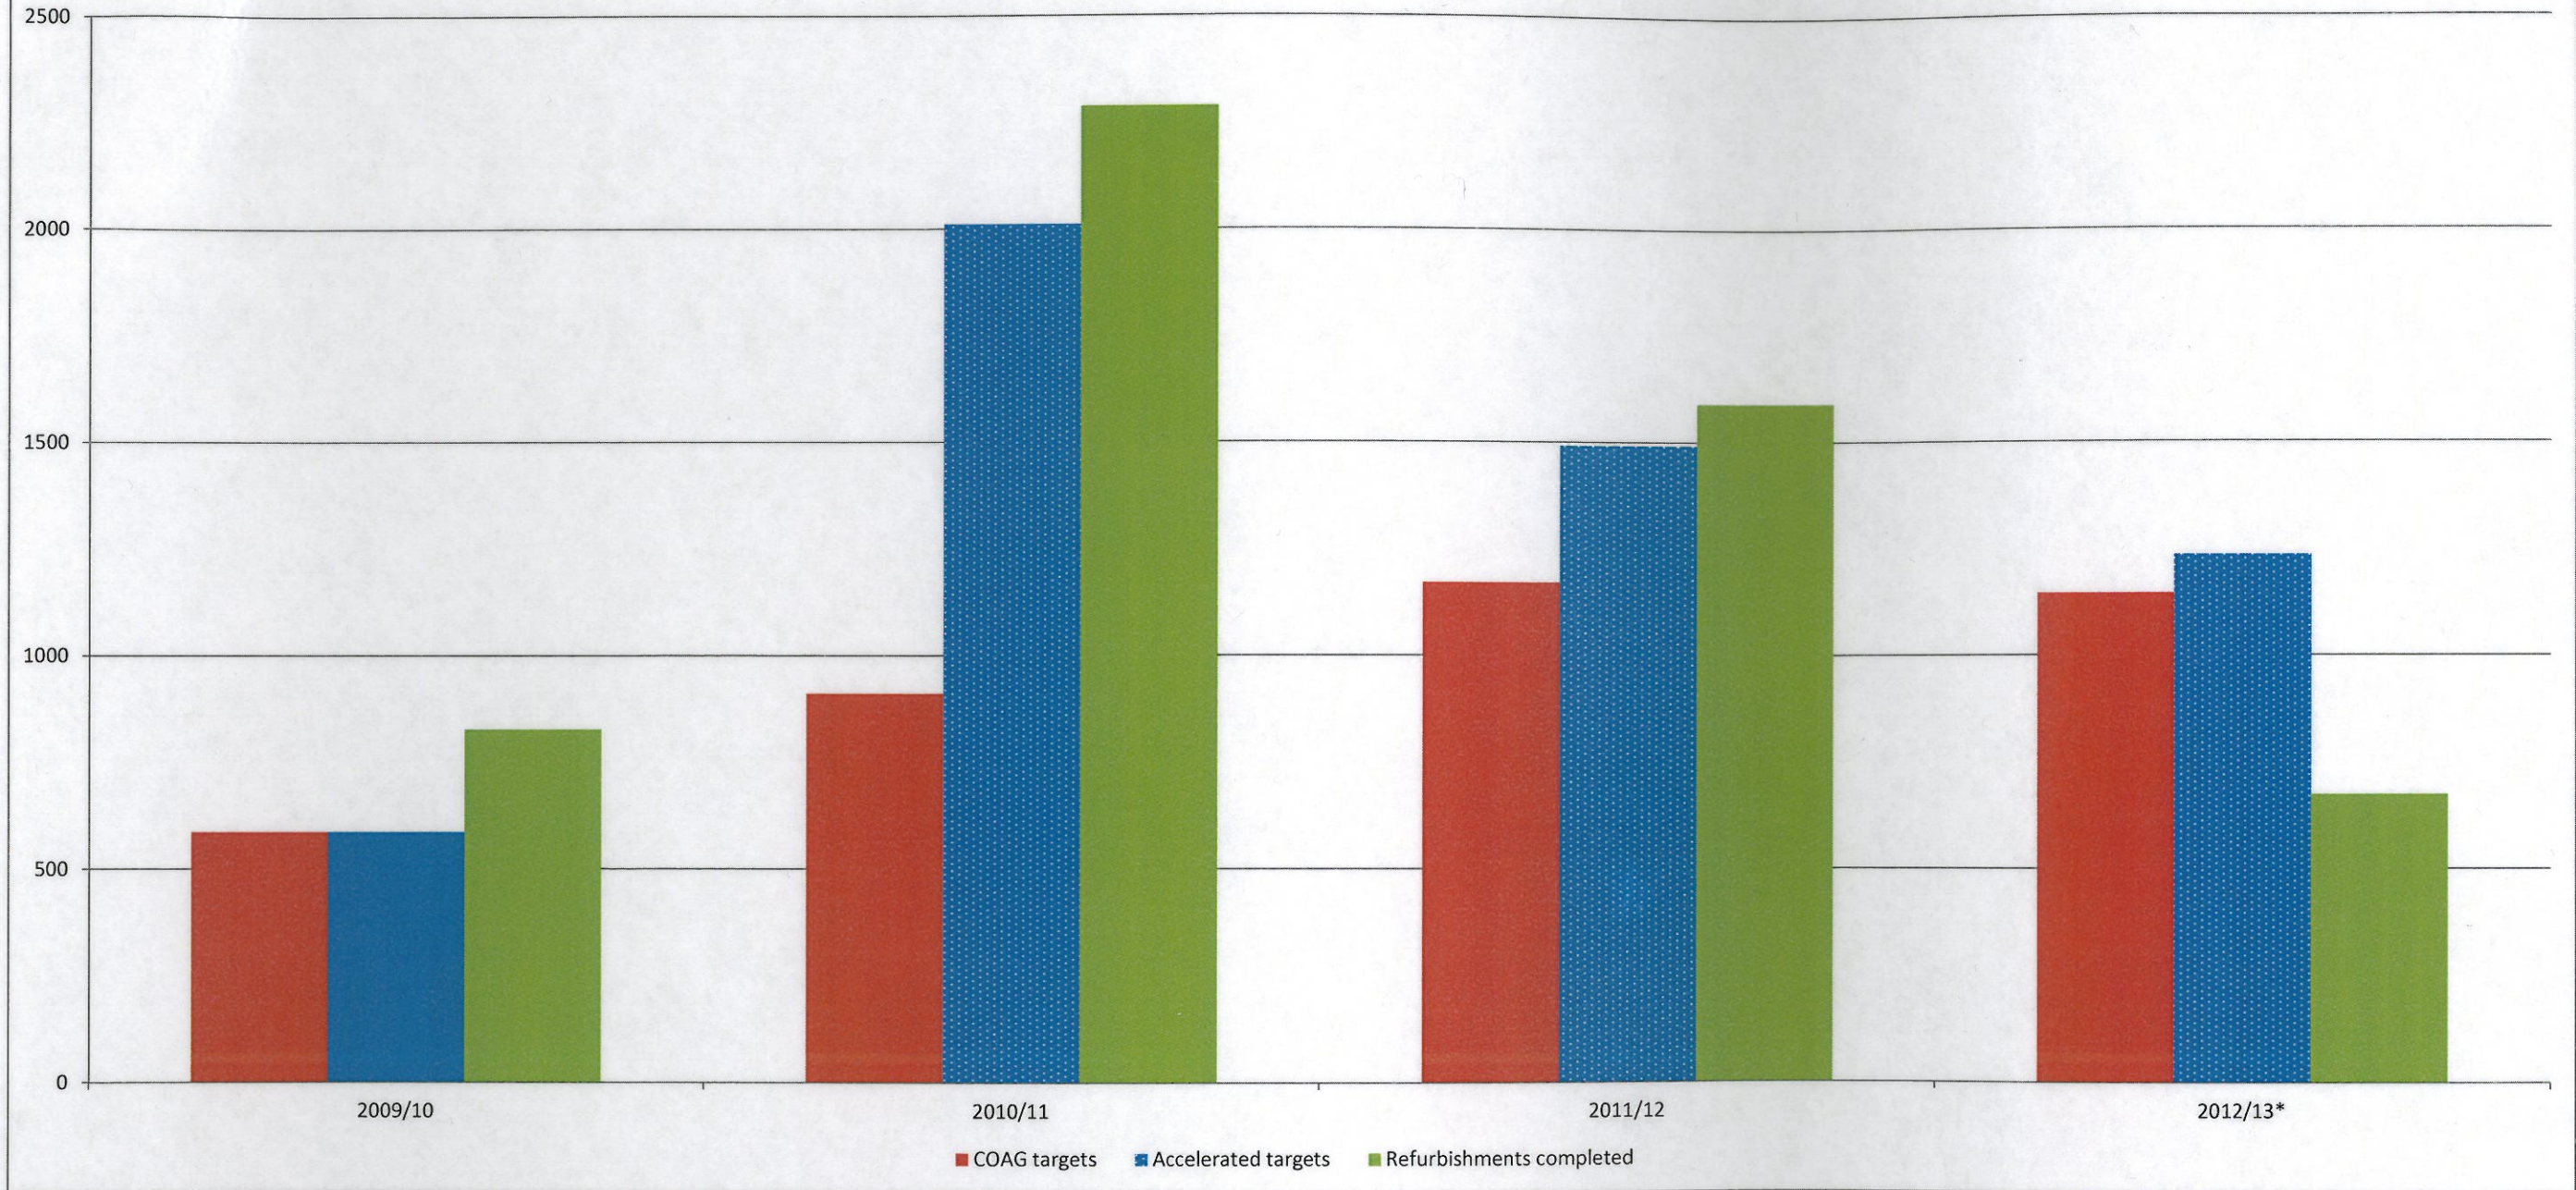


#### Refurbishments - yearly progress

	2009/10	2010/11	2011/12	2012/13*	2013/14
COAG targets	587	911	1171	1146	1061
Accelerated targets	587	2012	1493	1236	753
Refurbishments completed	828	2288	1591	674	

\*2012/13 denotes refurbishments completed and underway as at 31 December 2012.



## NPARIH PROGRESS - REFURBISHMENTS

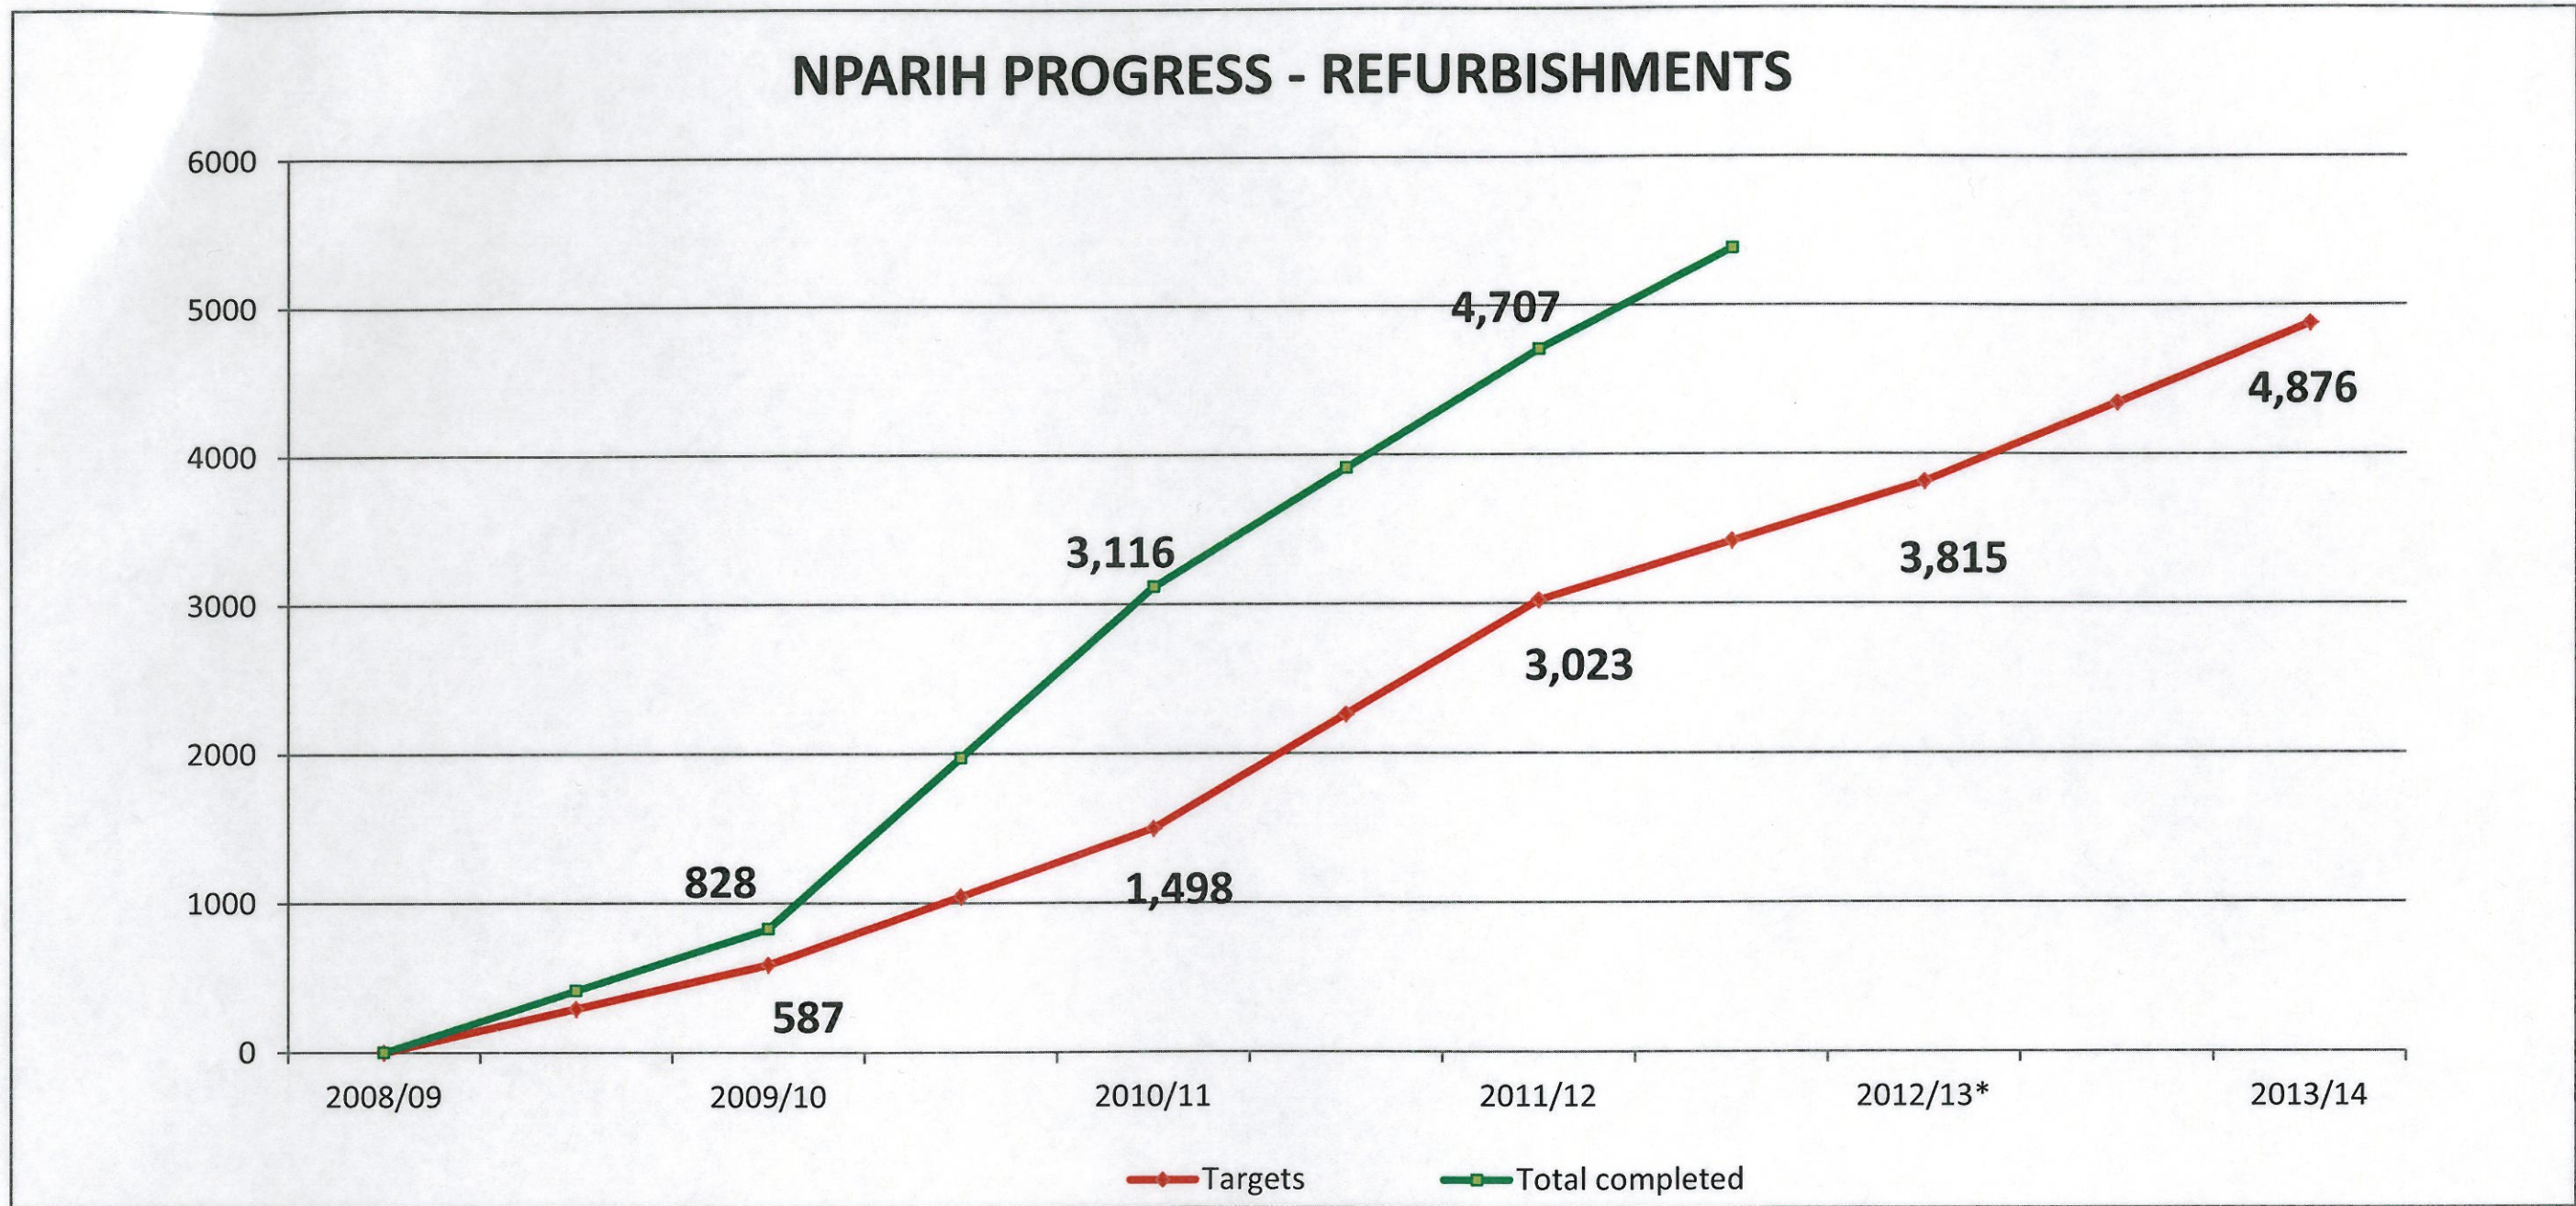


### Refurbishments

	2008/09	2009/10	2010/11	2011/12	2012/13*	2013/14	2014/15
<b>Targets</b>	0	587	1,498	3,023	3,815	4,876	
<b>Total completed</b>	0	828	3,116	4,707			

\*2012-13 refurbishments include those completed and underway as at 31 December 2012



## NPARIH NT PROGRESS - NEW HOUSES

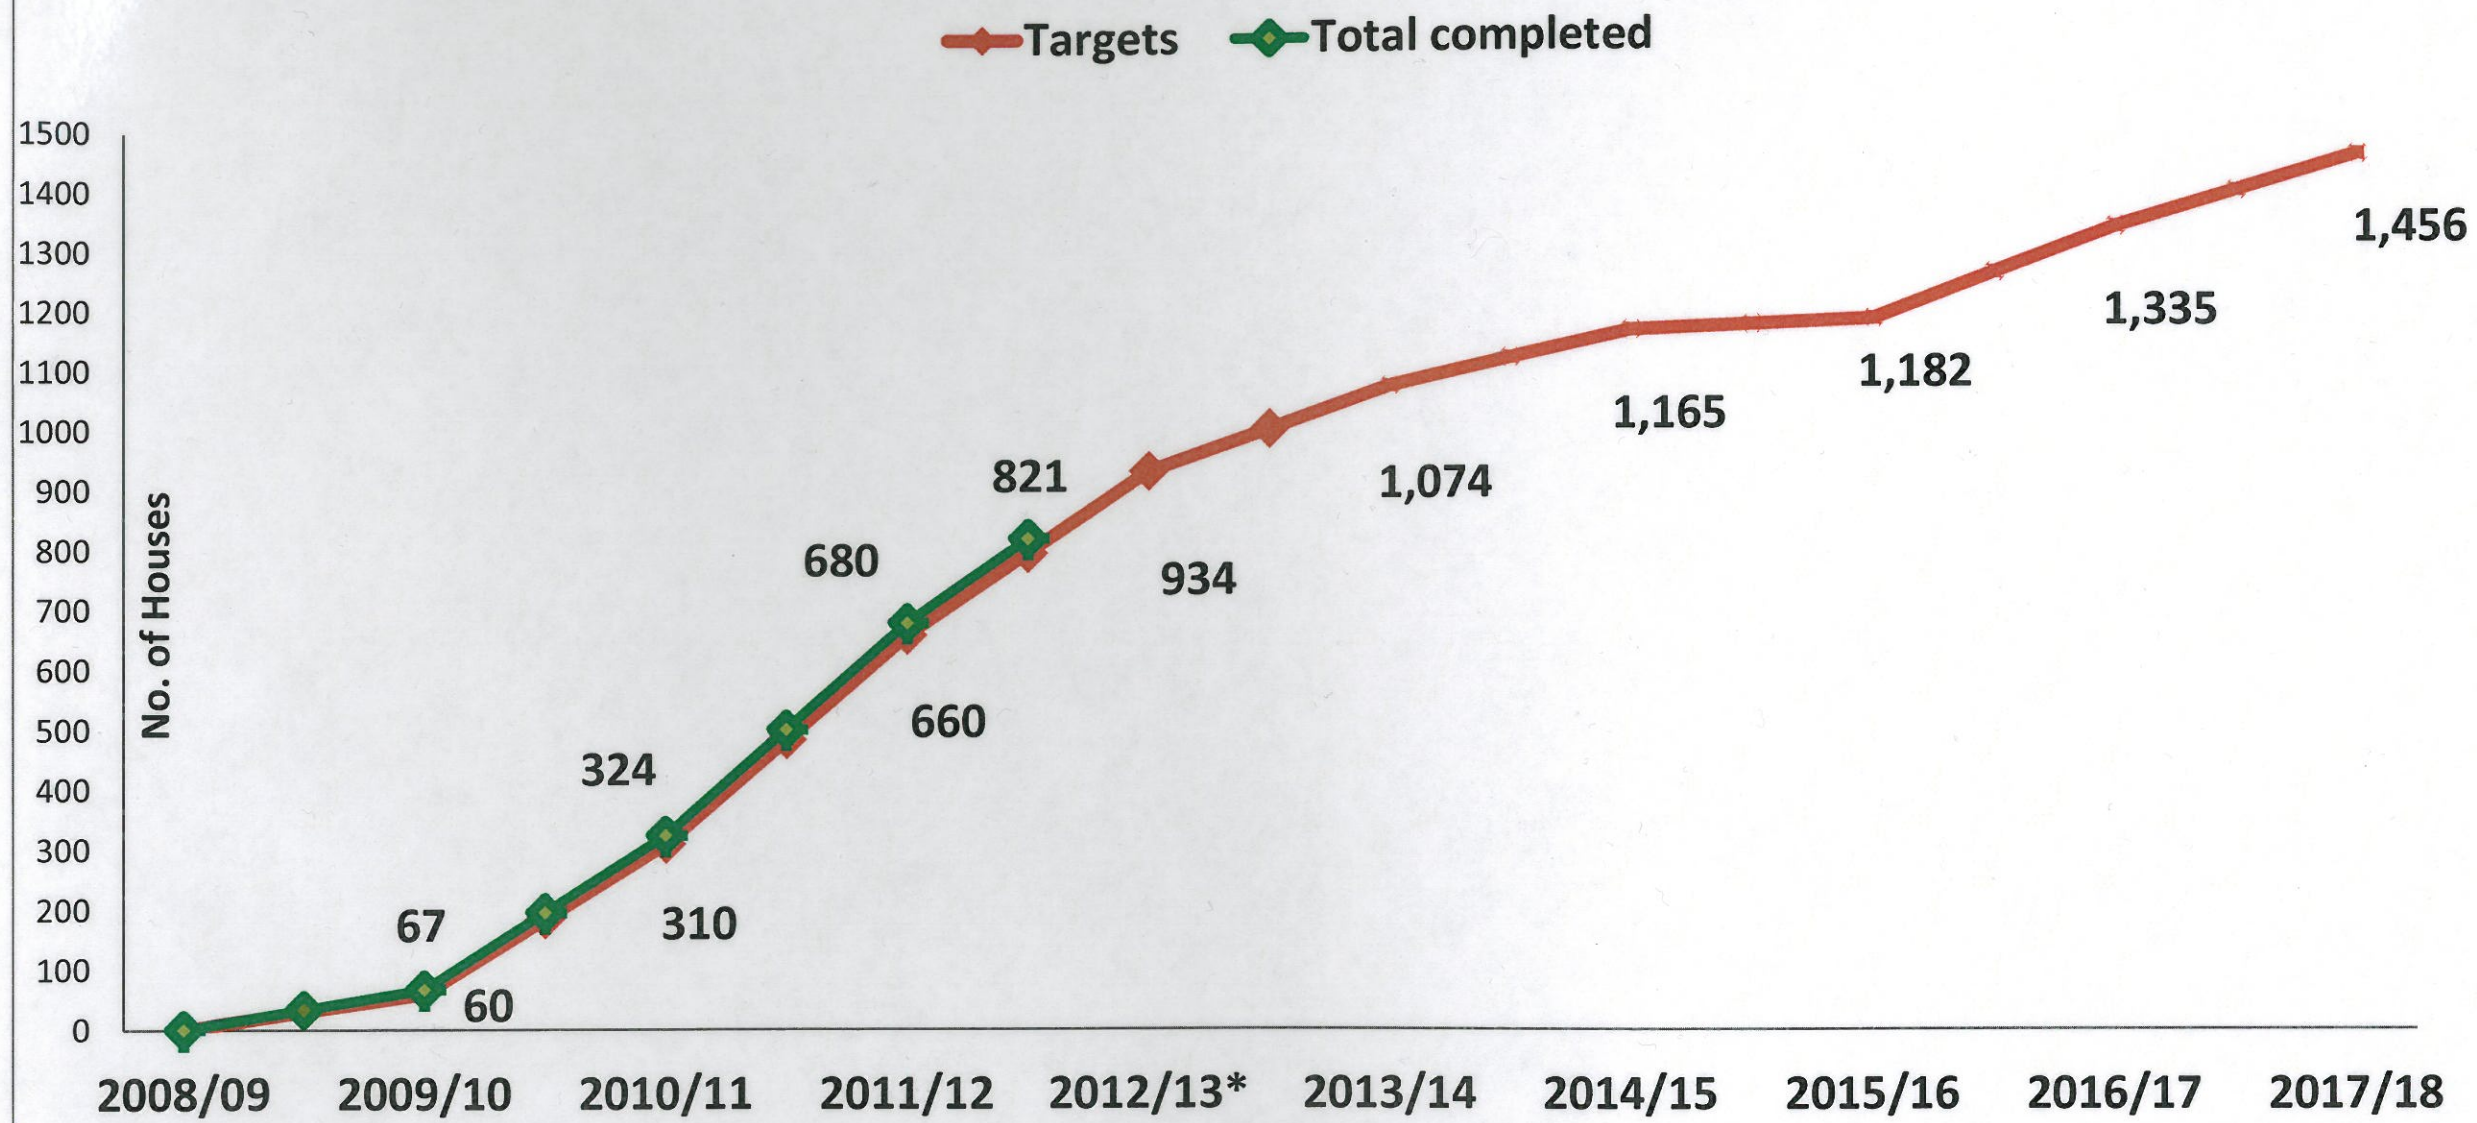


### New Houses

	2008/09	2009/10	2010/11	2011/12	2012/13*	2013/14	2014/15	2015/16	2016/17	2017/18
<b>Targets</b>	0	60	310	660	934	1,074	1,165	1,182	1,335	1,456
<b>Total completed</b>	0	67	324	680	821					

\*2012-13 data denotes new houses completed and underway as at 20 December 2012



## NPARIH PROGRESS - NEW HOUSES

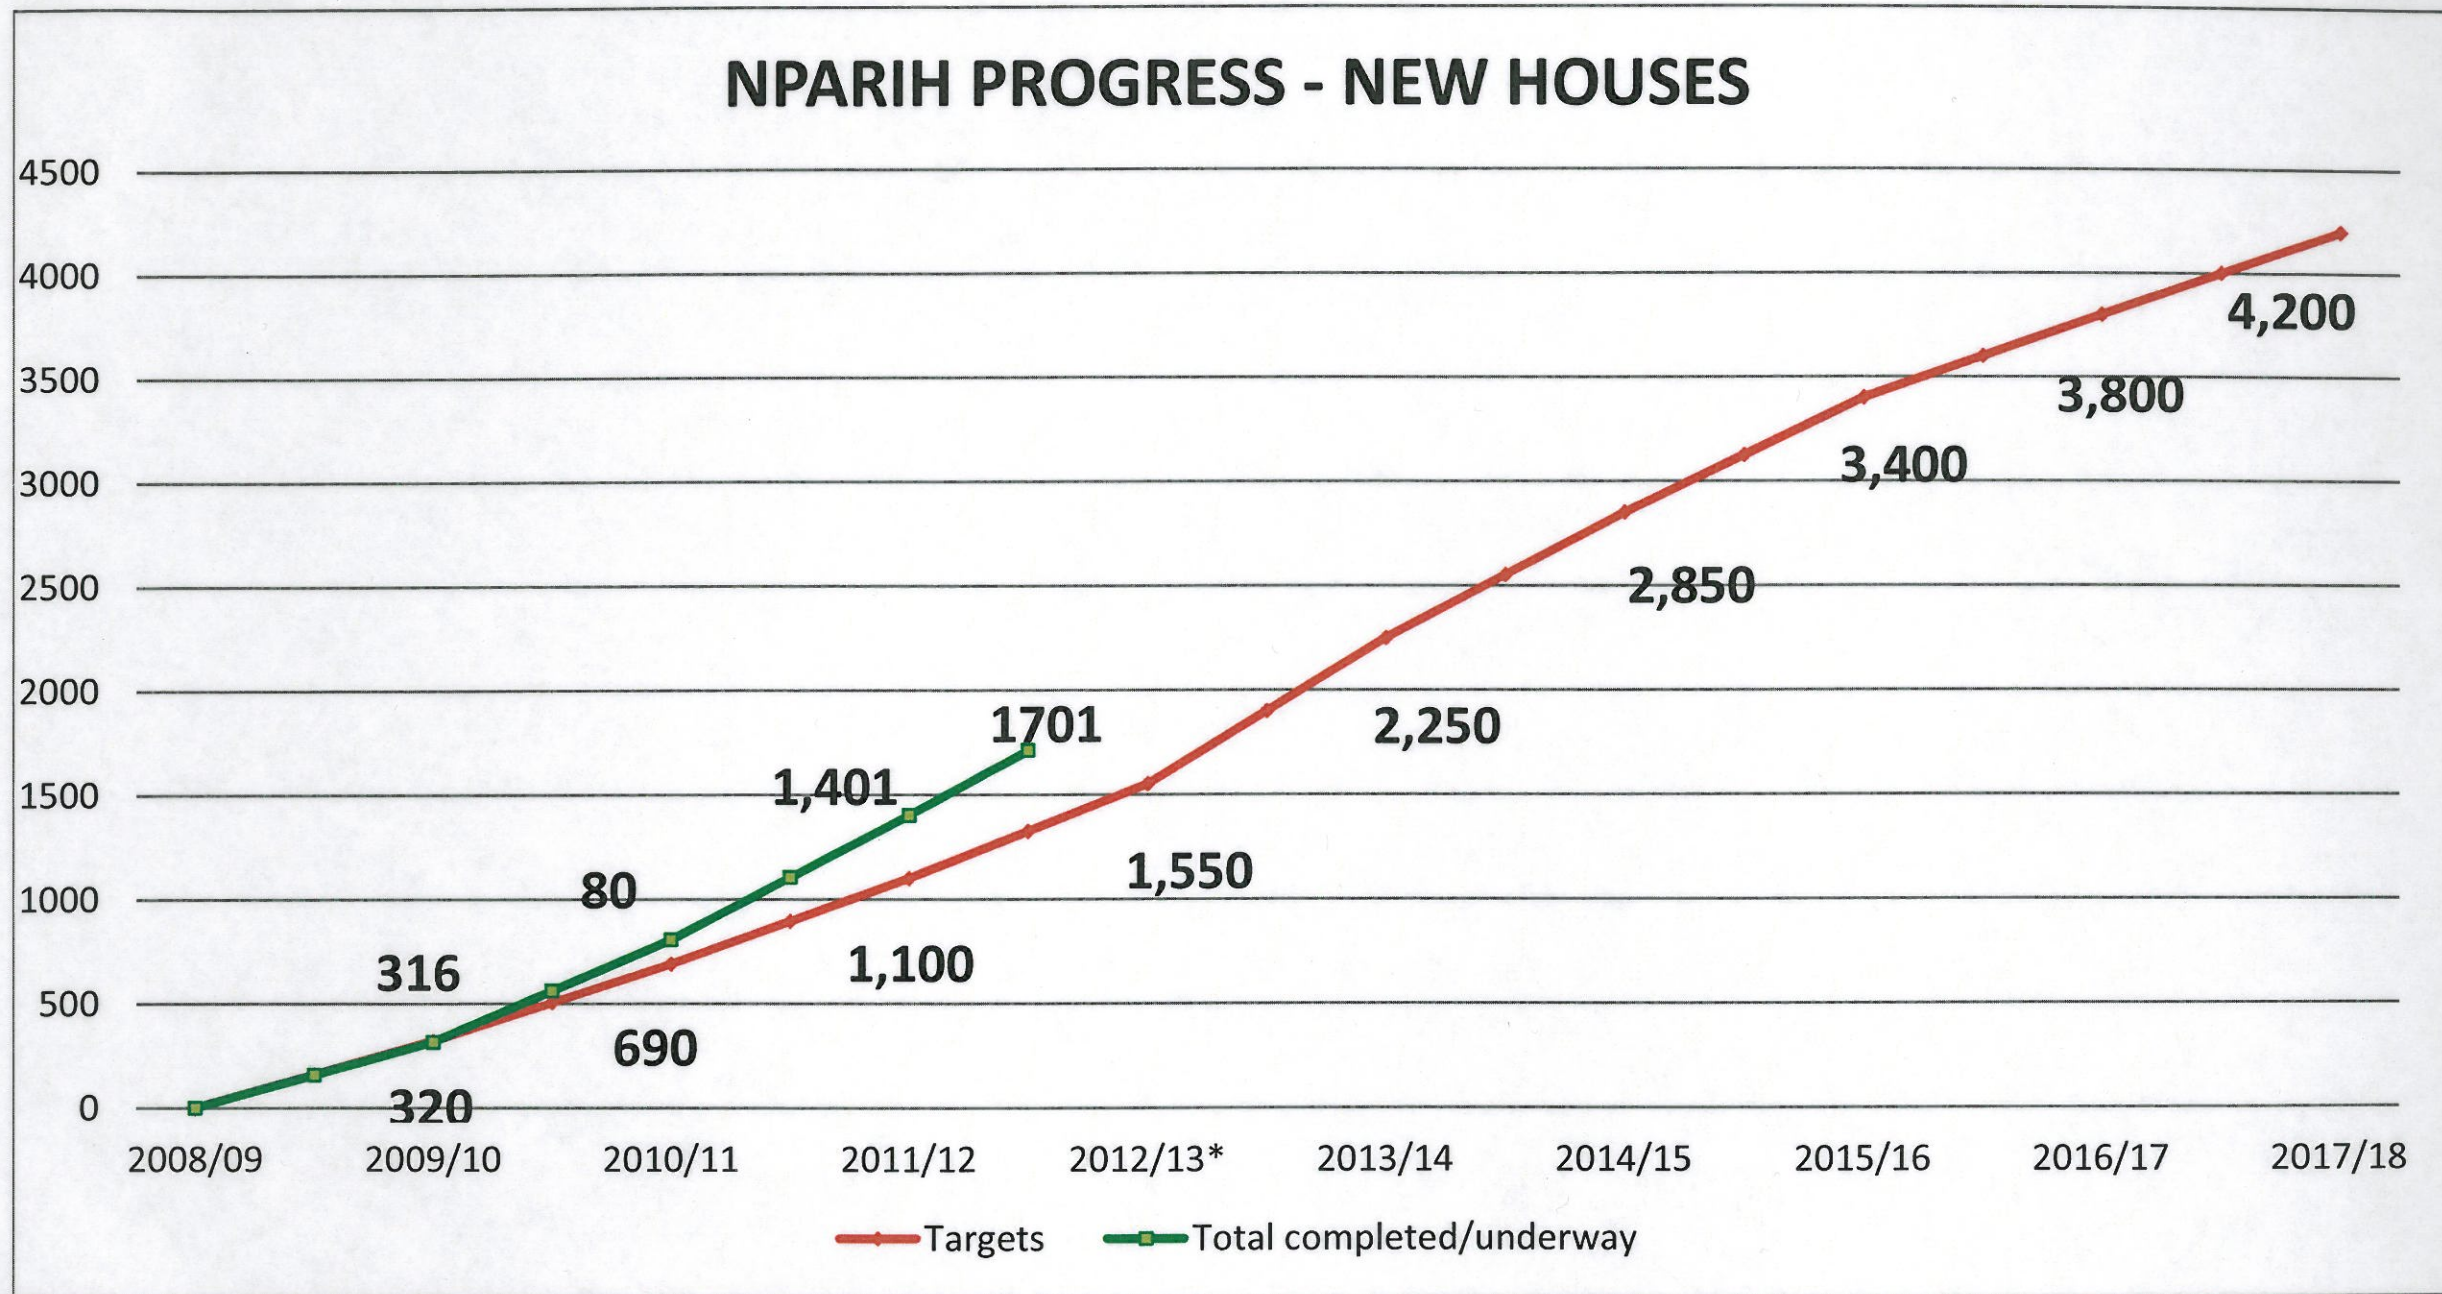


### New Houses

	2008/09	2009/10	2010/11	2011/12	2012/13*	2013/14	2014/15	2015/16	2016/17	2017/18
<b>Targets</b>	0	320	690	1,100	1,550	2,250	2,850	3,400	3,800	4,200
<b>Total completed/underway</b>	0	316	806	1,401	1,711					

\* 2012-13 data denotes new houses completed and underway as at 31 December 2012



### NPARIH NEW HOUSING - ANNUAL ACHIEVEMENTS

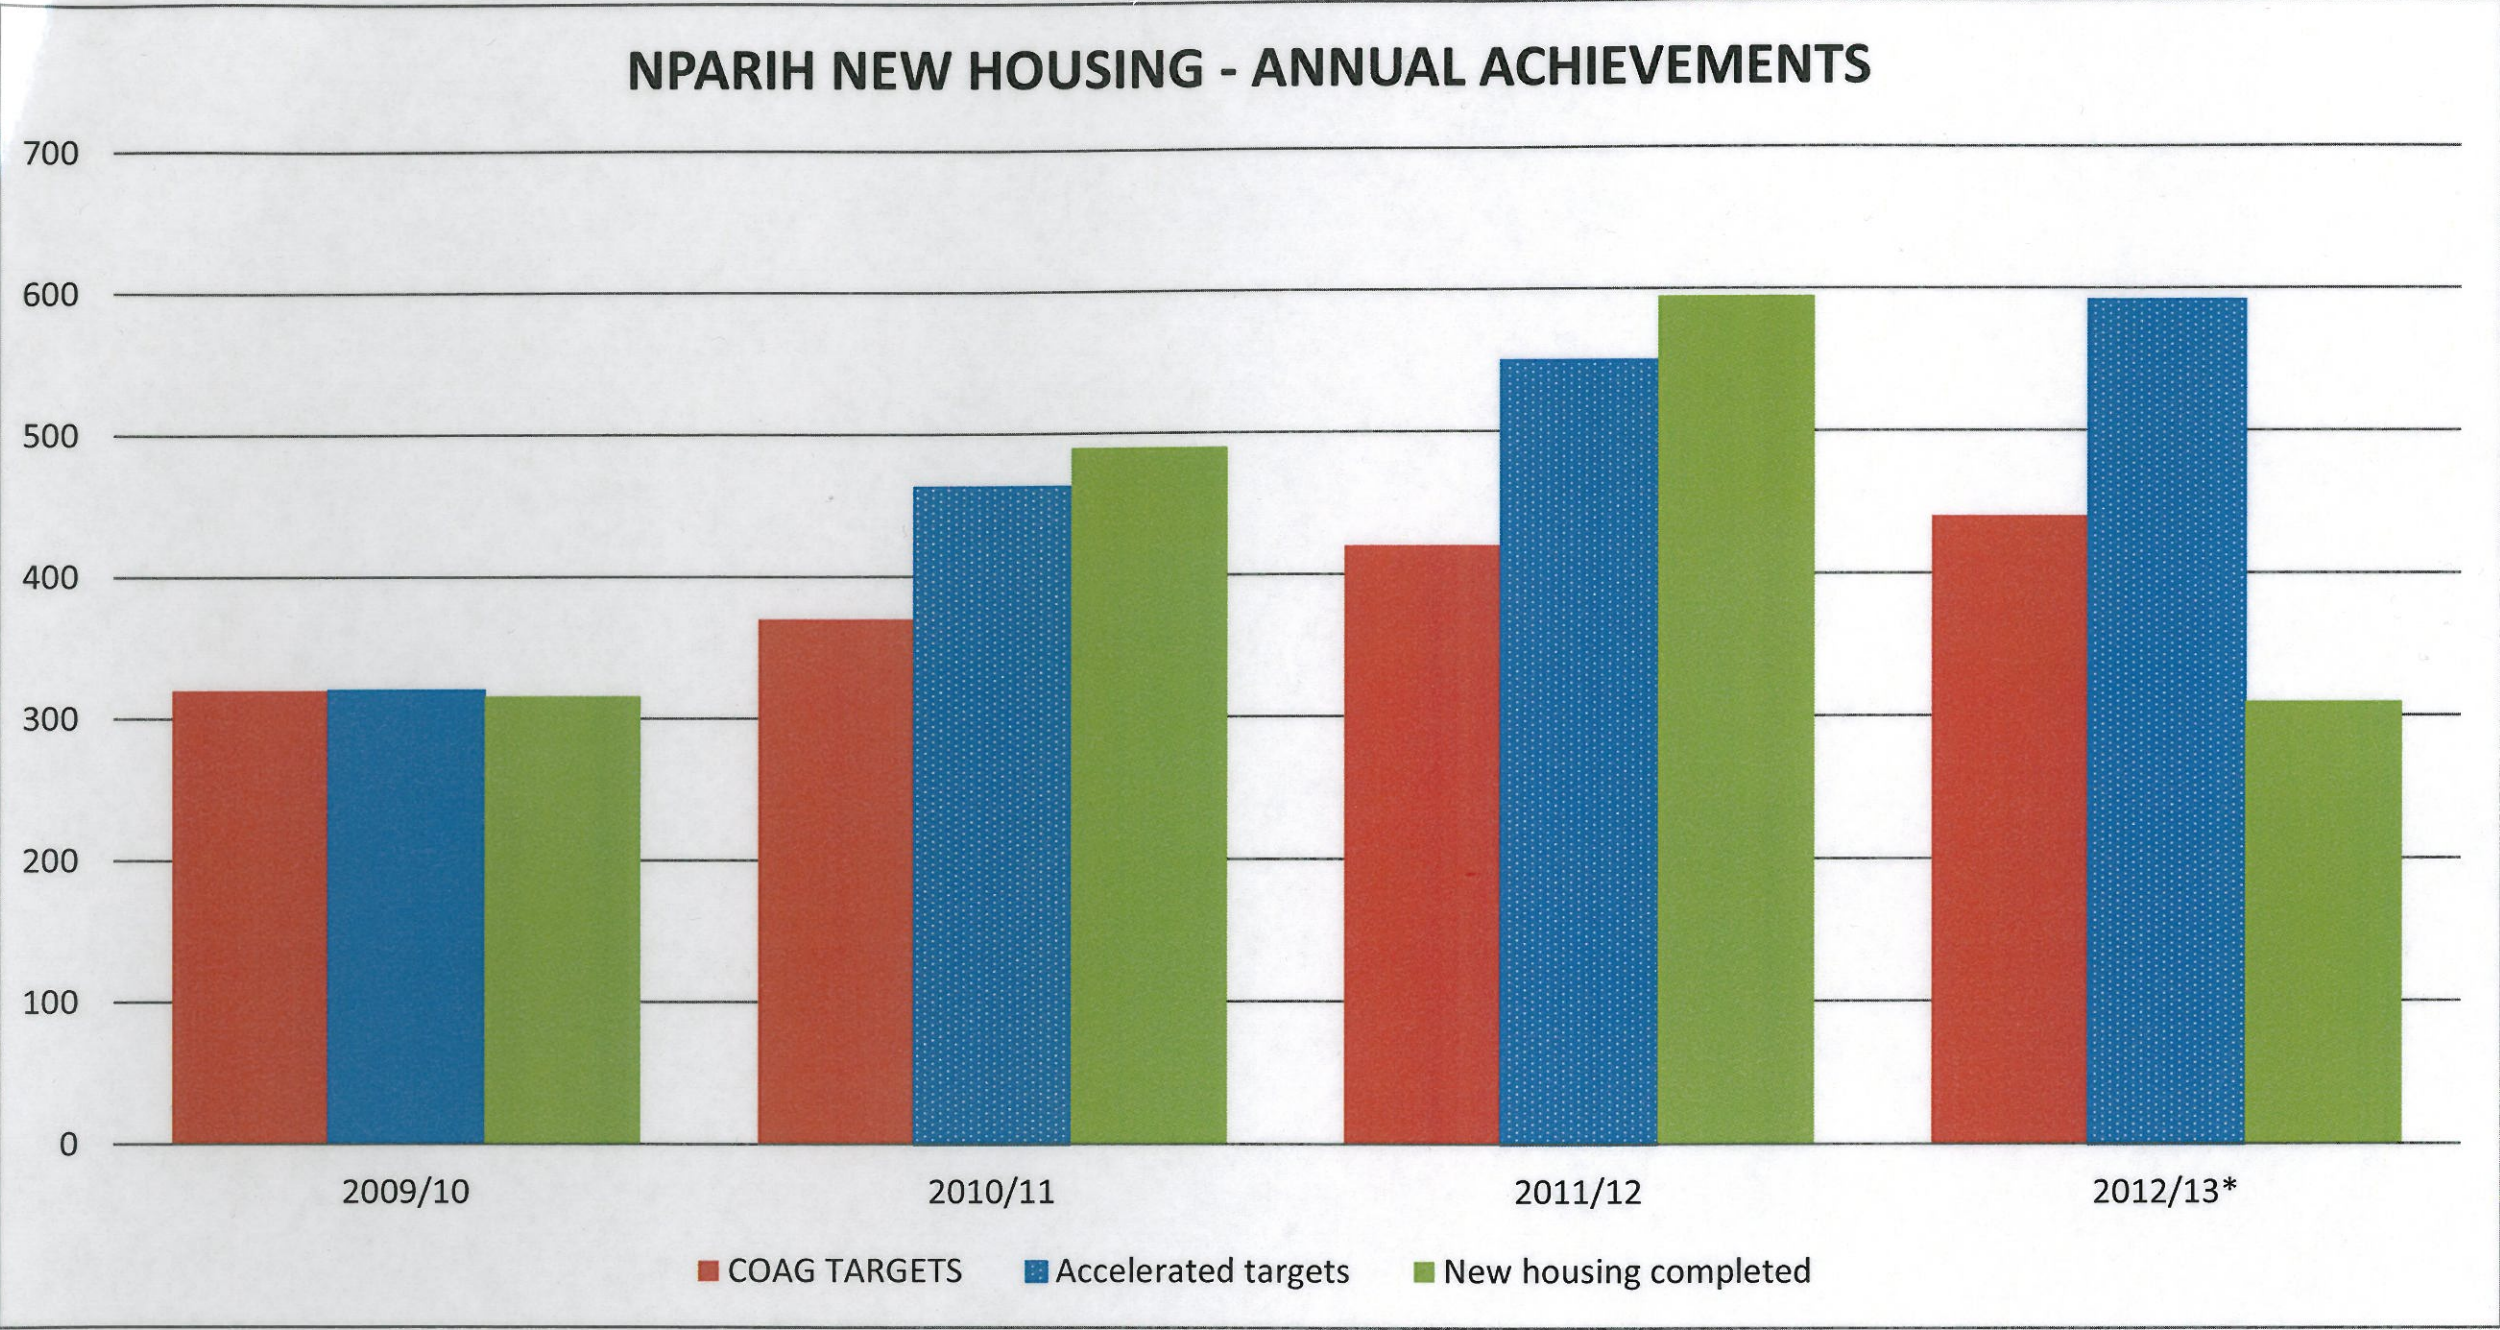


### New Housing

	2009/10	2010/11	2011/12	2012/13*	2013/14
<b>COAG TARGETS</b>	320	370	420	440	700
<b>Accelerated targets</b>	320	463	550	592	537
<b>New housing completed</b>	316	490	595	310	

\*2012/13 denotes new housing completed and underway as at 31 December 2012.



### NPARIH NT PROGRESS - REFURBISHMENTS

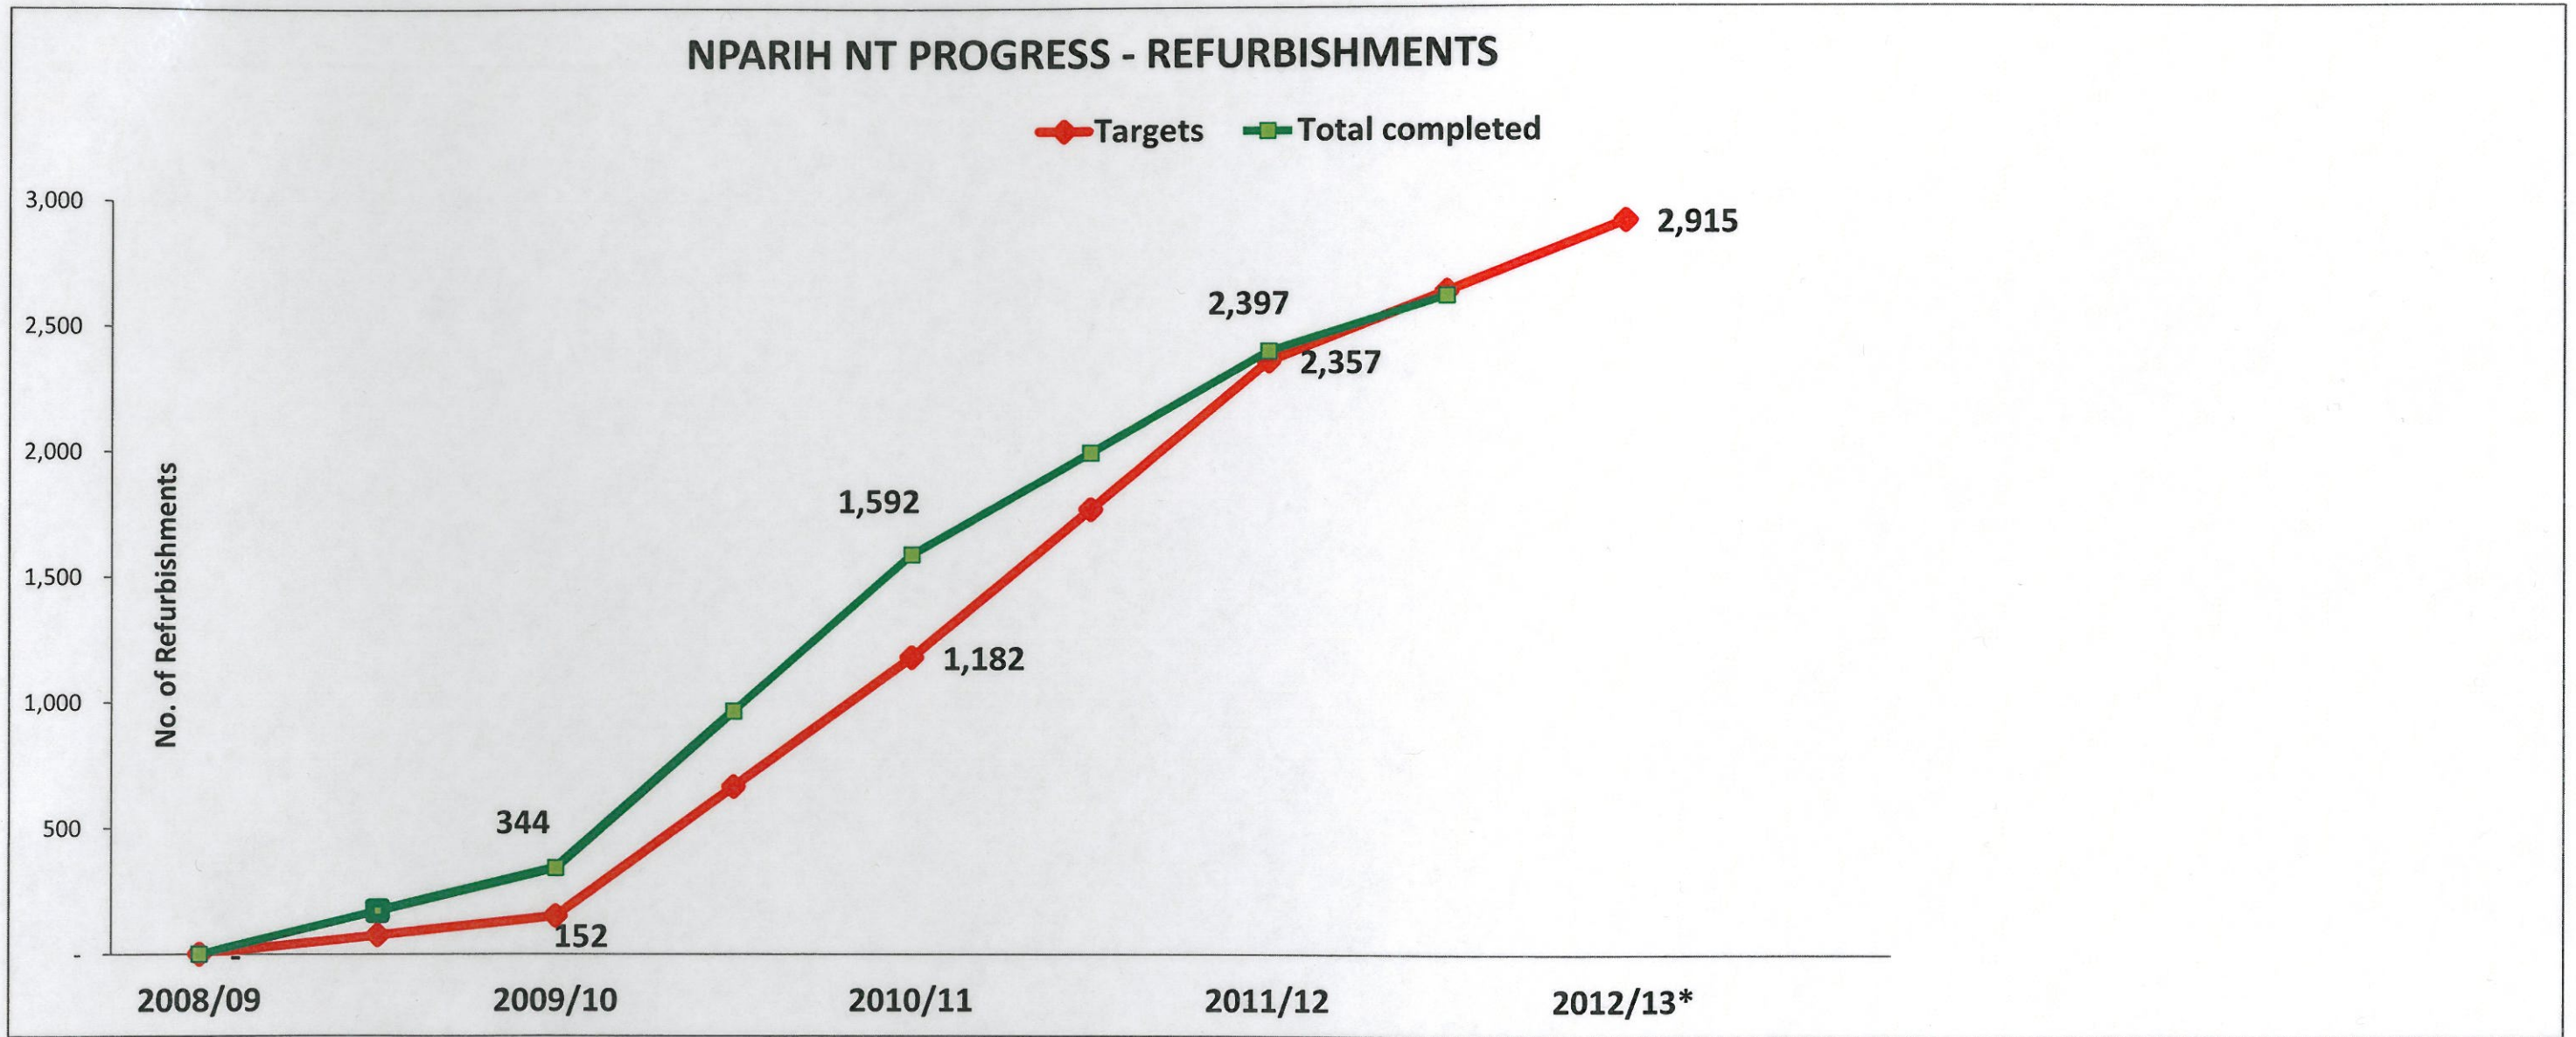

#### Refurbishments

	2008/09	2009/10	2010/11	2011/12	2012/13*
Targets	-	152	1,182	2,357	2,915
Total completed	-	344	1,592	2,397	

\*2012-13 data denotes refurbishments/rebuilds completed and underway as at 20 December 2012
